Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Student Name: Abdul Mateen Shaikh

SRN: PES1UG24AM332

Section: F

1. Lab Objective

Convert the functional requirements of the Subscription Detection & Analysis project into Agile backlog items (Epics and User Stories), prioritize and estimate them using the Fibonacci sequence (Planning Poker), simulate two 1-week sprints across workflow states (To Do → In Progress → Done), and analyze team progress and capacity using Jira's Burndown Chart.

2. Lab Deliverables & Screenshots

Deliverable 1: Jira Backlog with Epics and User Stories

ID	Type	Summary	Parent Epic	Priority	Story Points
SCRUM-6	Epic	Subscription Detection & Analysis	—	Medium	—
SCRUM-7	Epic	Alerts & Notifications	—	Medium	—
SCRUM-8	Epic	Expense Insights & Burn Rate	—	Medium	—
SCRUM-9	Epic	Subscription Cancellation	—	Medium	—
SCRUM-10	Epic	Finance Auditor Reporting	—	Medium	—
SCRUM-11	Story	Detect Recurring Billing Patterns	Subscription Detection & Analysis	High	8
SCRUM-12	Story	Classify Detected Subscriptions	Subscription Detection & Analysis	Medium	5
SCRUM-13	Story	Project Next Billing Dates	Subscription Detection & Analysis	Medium	3
SCRUM-14	Story	Send Subscription Renewal Alerts	Alerts & Notifications	High	5
SCRUM-15	Story	Configure Renewal Alert Preferences	Alerts & Notifications	Medium	3
SCRUM-16	Story	Calculate	Expense Insights	High	5

		Monthly Expense Burn Rate	& Burn Rate		
SCRUM-17	Story	View Expenses by Category	Expense Insights & Burn Rate	Medium	3
SCRUM-18	Story	Access Subscription Cancellation Guide	Subscription Cancellation	Medium	3
SCRUM-19	Story	Export Recurring Expense Report	Finance Auditor Reporting	Medium	5

TOTAL: 5 Epics + 9 Stories 40 Story Points

Backlog summary: SCRUM-6 is the main Subscription Detection & Analysis epic, with SCRUM-11 to SCRUM-13 as its child stories. The remaining epics cover alerts and notifications, expense insights, subscription cancellation, and finance auditor reporting.

Deliverable 2: Active Sprint Board (Sprint Simulation)

Sprint 1:

Sprint 1 focused on the core subscription-detection flow and renewal alerts. Stories: SCRUM-11 (8), SCRUM-12 (5), SCRUM-13 (3), SCRUM-14 (5). Total: 21 story points.

Workflow simulation: To Do → In Progress → Done. All Sprint 1 stories were completed and moved to Done.


Sprint 2:

Sprint 2 focused on expense analysis, cancellation guidance, and finance reporting. Stories: SCRUM-15 (3), SCRUM-16 (5), SCRUM-17 (3), SCRUM-18 (3), SCRUM-19 (5). Total: 19 story points.

Workflow simulation: To Do → In Progress → Done. All Sprint 2 stories were completed and moved to Done.


Deliverable 3: Sprint Burndown Chart

Sprint 1:

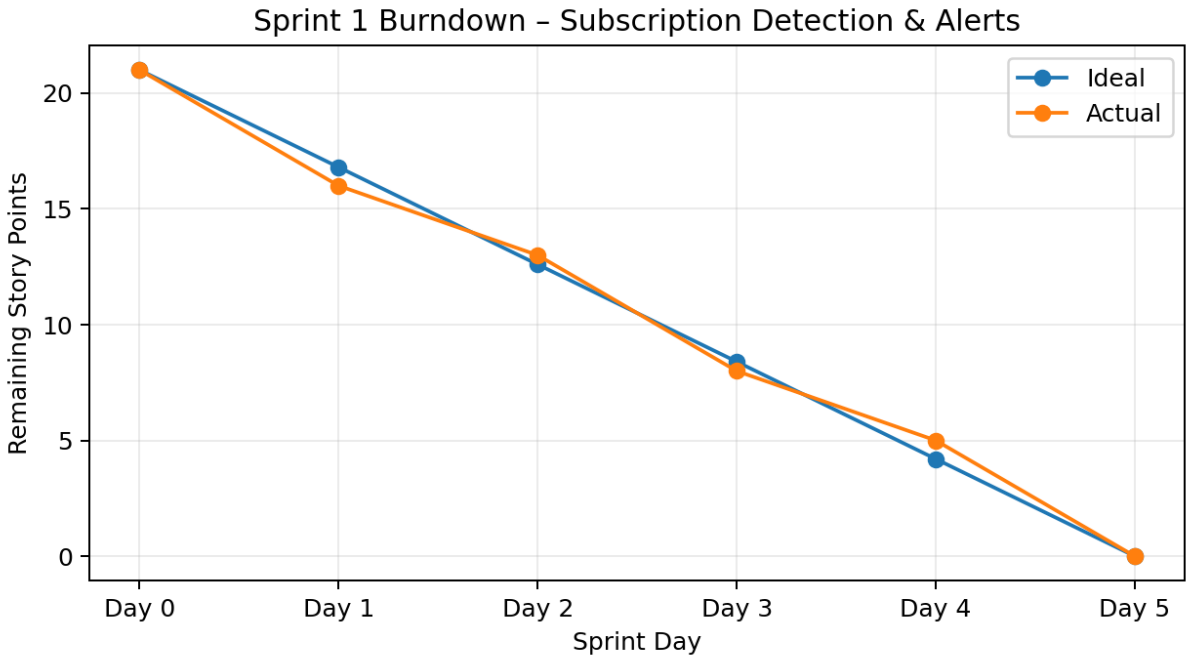

Sprint 1 planned capacity: 21 story points.

Sprint 2:

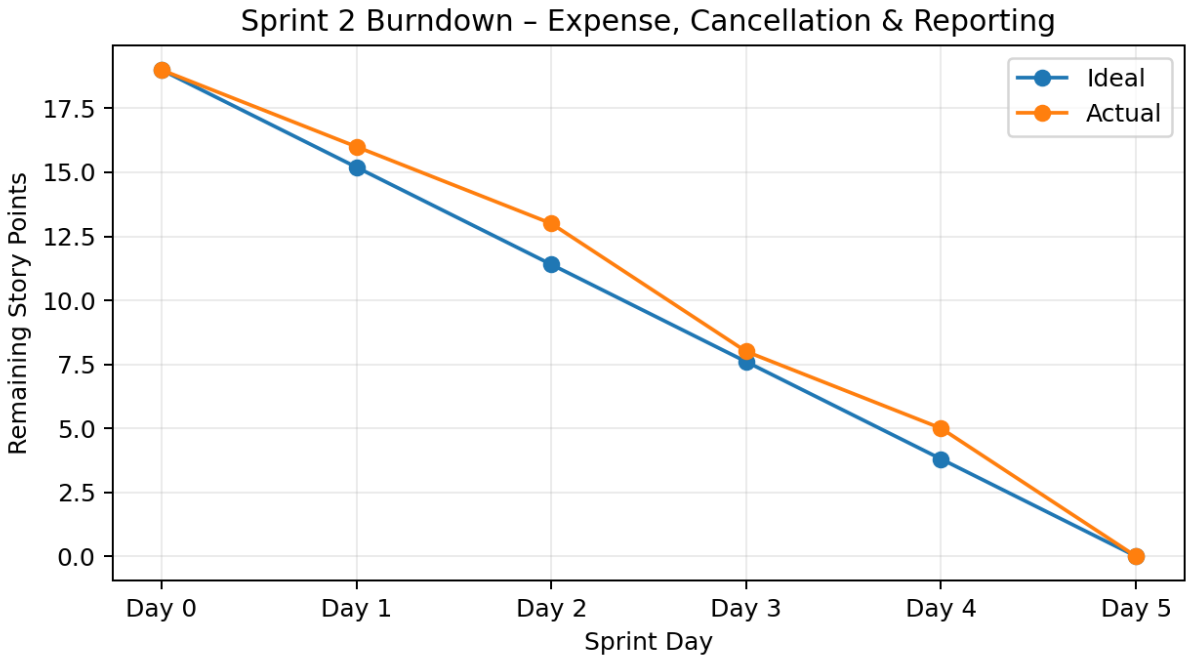

Sprint 2 planned capacity: 19 story points.

4. Sprint Reflection & Analysis

1. Did your estimations reflect the actual effort?

Answer: Yes. The story-point estimates reasonably reflected the relative effort and complexity of the work. The recurring billing-pattern detection story was assigned 8 points because it involves analyzing transaction history and identifying recurring patterns. Medium-complexity features such as subscription classification, renewal alerts, expense burn-rate calculation, and report export were assigned 5 points, while focused features such as billing-date projection, alert preferences, expense grouping, and cancellation guidance were assigned 3 points.

2. Was your backlog well-prioritized?

Answer: Yes. The backlog was prioritized according to functional importance. High-priority features such as recurring billing detection, renewal alerts, and expense burn-rate calculation were placed before supporting medium-priority features such as classification, billing-date projection, alert preferences, expense grouping, cancellation guidance, and finance reporting.

3. How did your simulated sprint align with your plan?


Answer: The simulated sprints followed the planned development flow. Sprint 1 focused on subscription detection and renewal-alert functionality, while Sprint 2 focused on expense analysis, subscription cancellation guidance, and finance reporting. The stories were moved through To Do → In Progress → Done to demonstrate the sprint workflow.

4. What insights did the burndown chart give about your team's capacity?

Answer: The burndown charts showed how the remaining story points decreased as work items were completed. Sprint 1 contained 21 story points and Sprint 2 contained 19 story points, for a total planned workload of 40 story points. Because the sprints were simulated for the lab, the charts demonstrate the relationship between completed work, remaining workload, and planned team capacity rather than representing actual long-term development velocity.


Jira project reference: SCRUM-6 – Subscription Detection & Analysis. The backlog and issue hierarchy were prepared from the Jira work items for this project.

Deliverable 1 – Jira Epics

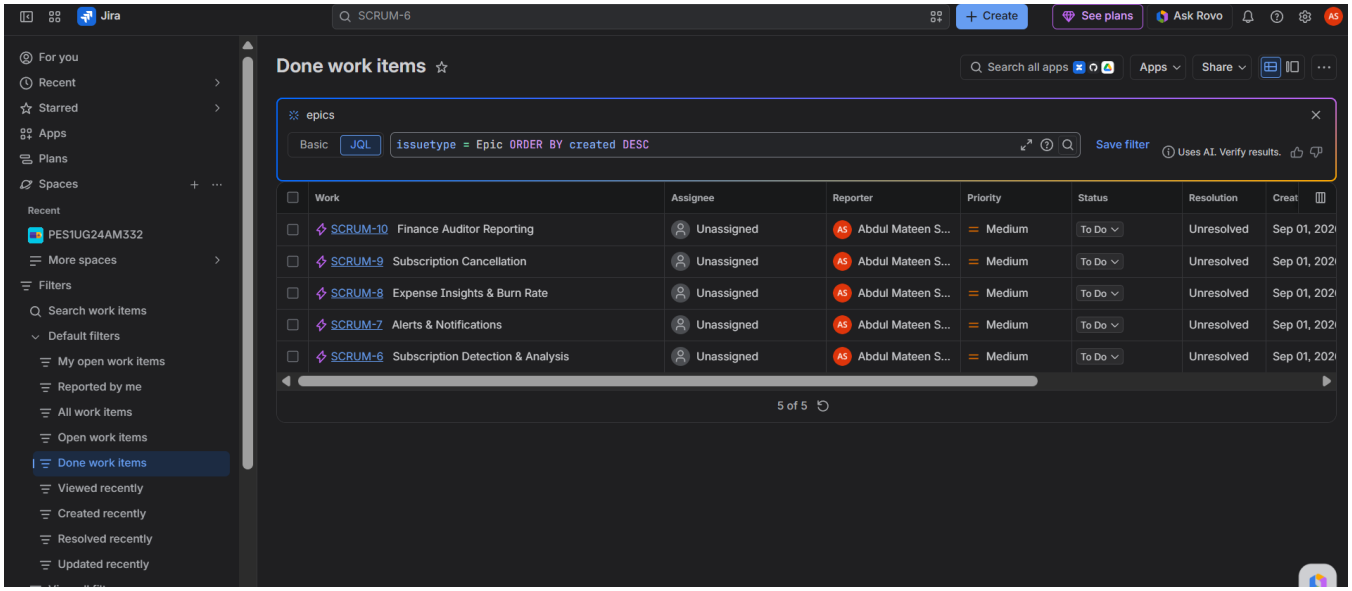


Jira view showing the five project epics, including SCRUM-6 Subscription Detection & Analysis.

Deliverable 2 – Sprint 1

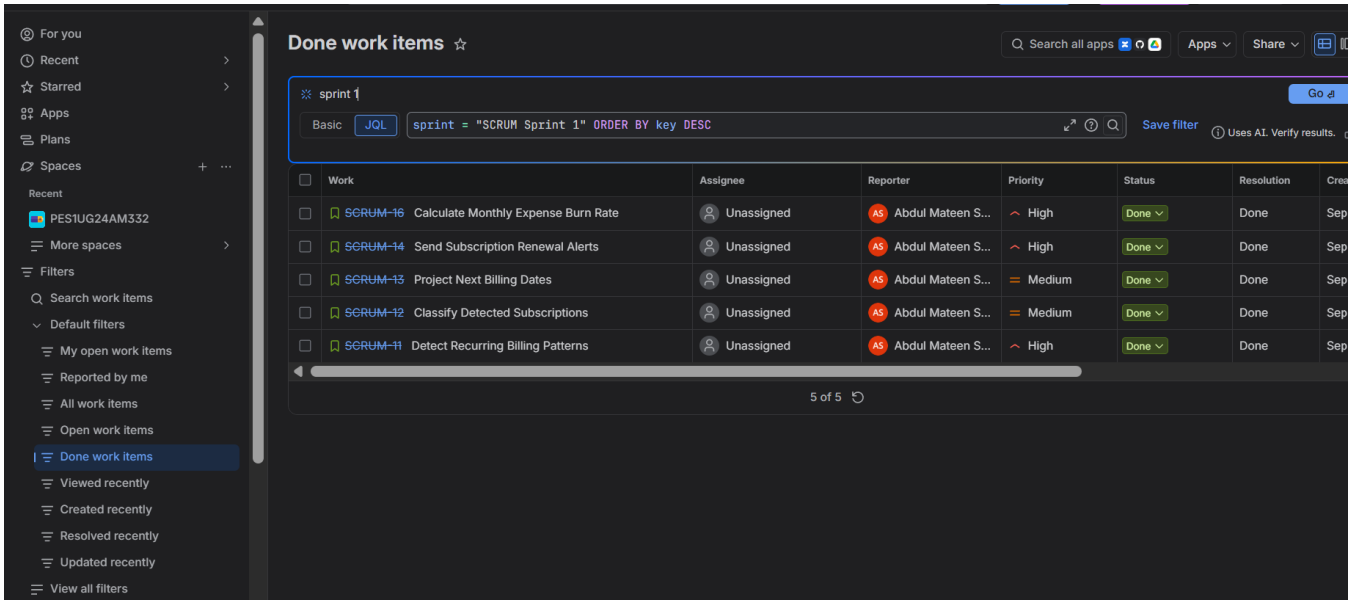

Jira Done Work Items view filtered for Sprint 1, showing the five completed Sprint 1 stories.

Deliverable 2 – Sprint 2

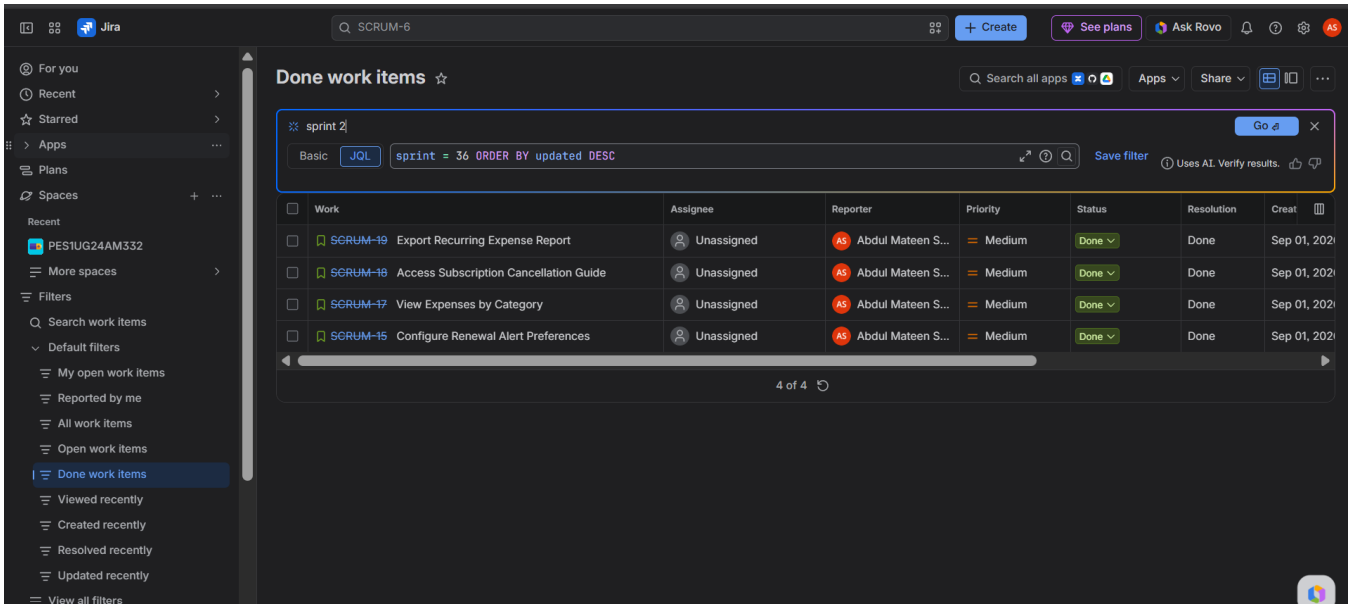

Jira Done Work Items view filtered for Sprint 2, showing the four completed Sprint 2 stories.
